
LAUNCH PLAN · MONTH ONE

Setting the Cosmo Circle in motion

2 November – 5 December 2026. By the end of the month Cosmo has a locked sales baseline, a code on every hero pack, a working WhatsApp verification line, a community lead in post, 100 founding members, 20+ creators selling on codes, and its first Lagos Glow Session. It spends about ₦10.6m of Phase 1's ₦23m.

Owners: CEO · Oladapo Olayinka (strategy lead) · Finance · Ops (GVS warehouse and logistics) · Legal · Creative · Community lead (from 23 Nov) · the WhatsApp provider.

THE MONTH AT A GLANCE

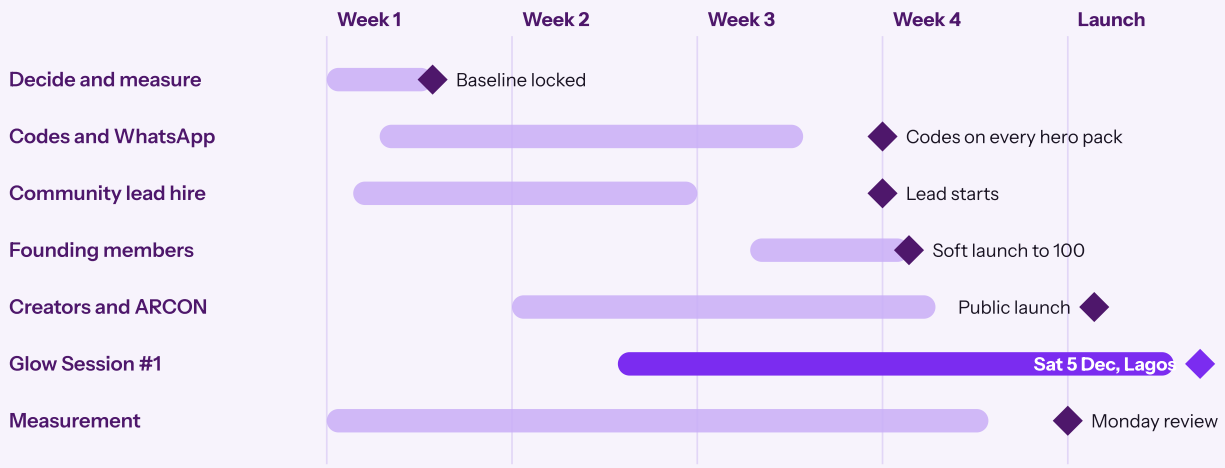

Bars show when each workstream is active; diamonds mark the milestone that closes it. Glow Session #1 on Sat 5 Dec ends the month.

DECIDE THIS WEEK

- **Approve Phase 1** (₦23m, November to January) and the Gate 1 targets for 31 January: 3,000 members, 30% of sales coded, ≤ ₦6,000 per new customer.
- **Name an interim owner** for the Circle until the community lead starts.
- **Send the letter to Sterling** on stickers, promotions and customer data. The sticker order on 10 November depends on the answer.
- **Reply to the ₦150m influencer** with a request for audience data and a price for one coded test post, instead of a yes or no.

WEEK 1 2–6 Nov

Decide and measure

	Task	Owner	Due	Done when
☐	Approve Phase 1: the ₦23m budget, the Gate 1 targets and the decision not to pay ₦150m upfront	**CEO, Oladapo**	Mon 2 Nov	Signed one-page approval
☐	Name an interim owner for the Circle until the community lead starts	**CEO**	Mon 2 Nov	Owner announced to the team
☐	Pull the baseline: six months of revenue, orders, average order, repeat rate, and sales by city and channel	**Finance**	Fri 6 Nov	Baseline sheet locked; no edits after
☐	Work out landed cost and margin per product after freight and duty	**Finance, Ops**	Fri 6 Nov	Real margins replace the 45% assumption
☐	Ask Sterling in writing whether GVS can add code stickers, run promotions and collect customer data	**CEO**	Send Tue 3 Nov; reply by Mon 9 Nov	Written yes, or a fallback agreed
☐	Pick 3–5 hero products and confirm each one's NAFDAC number	**Oladapo, Ops**	Fri 6 Nov	Hero list with NAFDAC numbers
☐	Request three quotes each for scratch-code stickers and a WhatsApp Business API provider	**Ops**	Wed 4 Nov	Six quotes in hand
☐	Advertise the community lead role; ask applicants for a one-page plan to grow a Lagos beauty community	**CEO, Oladapo**	Tue 3 Nov	Ad live; 10+ applicants by Mon 9 Nov
☐	Ask the ₦150m influencer's team for audience data and a price for one coded test post	**CEO**	Fri 6 Nov	Audience location, fake-follower share and test price received
☐	Collect results from the micro creators already used, and rank them	**Oladapo**	Fri 6 Nov	Ranked list of creators to keep
☐	Count October mentions of Cosmo on X, TikTok and Instagram	**Oladapo**	Fri 6 Nov	Social listening baseline recorded

WEEK 2 9–13 Nov

Build the machine

	Task	Owner	Due	Done when
☐	Choose the sticker printer and WhatsApp provider; order 20,000 unique codes	**Ops**	Tue 10 Nov	Purchase orders signed; delivery date confirmed
☐	Design the sticker: code, “Scratch and send to WhatsApp to verify”, NAFDAC number	**Creative**	Wed 11 Nov	Print-ready file approved
☐	Build the WhatsApp flow: code in, “genuine” reply, consent, welcome, points	**Oladapo, provider**	Fri 13 Nov	Works end to end on a test phone
☐	Set up the customer list keyed on phone number: name, city, product, code, source, consent	**Oladapo**	Fri 13 Nov	Sheet or CRM ready, tested
☐	Write the Circle rules: tiers, 5% points, ₦2,000 referral credit, 10% Ambassador commission, two broadcasts a week at most, privacy notice	**Oladapo, Legal**	Fri 13 Nov	One-page rules approved by the CEO

	Task	Owner	Due	Done when
☐	Interview the five shortlisted community lead candidates	**CEO, Oladapo**	Thu 12–Fri 13 Nov	Preferred candidate chosen
☐	Book Glow Session #1 in Lagos for Sat 5 Dec (40–60 seats) and a dermatologist	**Oladapo**	Fri 13 Nov	Venue and dermatologist confirmed in writing
☐	Sign 20–25 micro creators for December on base fee plus commission; give each a unique code	**Oladapo**	Fri 13 Nov	Terms signed; codes issued
☐	Submit the core campaign creative to ARCON for vetting	**Legal**	Fri 13 Nov	Submission receipt

WEEK 3 **16–20 Nov**

Test and recruit

	Task	Owner	Due	Done when
☐	Make the community lead offer, with a start date of Mon 23 Nov	**CEO**	Mon 16 Nov	Offer accepted
☐	Receive the stickers and apply them to all hero stock in the warehouse	**Ops**	Fri 20 Nov	Every hero pack leaving from 23 Nov carries a code
☐	Test end to end: 20 people buy, scratch, verify and receive points	**Oladapo, provider**	Thu 19 Nov	19 of 20 verify in under a minute; bugs fixed
☐	Invite 100 founding members: past buyers, creators' most engaged followers, staff networks	**Oladapo**	Wed 18 Nov	100 personal invitations sent
☐	Set founding perks: founding badge, double points in December, first seats at Glow Session #1	**Oladapo**	Wed 18 Nov	Perks named in the invitation
☐	Price the December gift bundles and an entry-price mini or trial kit	**Oladapo, Finance**	Fri 20 Nov	Prices set; margins checked
☐	Open Glow Session #1 tickets (₦5,000, returned as a voucher) to founding members	**Oladapo**	Fri 20 Nov	Ticket link live
☐	List 10 vendors and salons already selling Cosmo as future verified resellers	**Ops**	Fri 20 Nov	List with contacts

WEEK 4 23–27 Nov

Soft launch

	Task	Owner	Due	Done when
☐	Community lead starts; hand over the rules, customer list, WhatsApp flow and creator roster	**CEO, Oladapo**	Mon 23 Nov	Lead running daily tasks
☐	Open the WhatsApp community to founding members	**Community lead**	Tue 24 Nov	100 founding members in
☐	Creators go live with their codes, using ARCON-approved creative	**Community lead**	Wed 25 Nov	First coded orders recorded
☐	Hold the first live skin Q&A with the dermatologist	**Community lead**	Thu 26 Nov	Held; questions logged for content
☐	Switch on referral credit for members	**Oladapo**	Thu 26 Nov	First referral redeemed
☐	Build weekly dashboard v1: members, coded sales, cost per customer, creator cost per order	**Oladapo**	Fri 27 Nov	Dashboard shared with the CEO
☐	Write the Glow Session #1 run-sheet: agenda, consultations, trials, members-only bundle, photographer, photo consent	**Community lead**	Fri 27 Nov	Run-sheet signed off

LAUNCH WEEK 30 Nov–5 Dec

Go public

	Task	Owner	Due	Done when
☐	First Monday dashboard review	**CEO, Oladapo**	Mon 30 Nov	Actions agreed for the week
☐	Public launch: “Is it original? Verify it.” on TikTok and Instagram	**Creative, Community lead**	Tue 1 Dec	Posts live; ₦0.5m boost on the best member content
☐	Put December gift bundles on sale for the festive season	**Ops**	Tue 1 Dec	In stock online and with resellers
☐	Glow Session #1, Lagos	**Community lead, Oladapo**	Sat 5 Dec	40+ attendees; sales recorded on codes
☐	Write the month-one report against the scorecard	**Oladapo**	Mon 7 Dec	Report shared with the CEO

END OF MONTH ONE

The month-one scorecard

Review it at the Monday meeting on 7 December. Month one puts the machine in place; Gate 1 on 31 January is where the money for Phase 2 is decided.

Measure	Target by 5 Dec	Gate 1, 31 Jan 2027
Baseline locked	Yes, by 6 Nov	—
Hero packs carrying a code	100% from 23 Nov	100%
Verified members	500	3,000
Founding members in the community	100	—
Creators live on codes	20+	20–25
Share of sales carrying a code	10% (first reading)	30%
Glow Session #1 tickets sold	40+	—
ARCON approval for core creative	Received	—
Community lead in post	Yes, from 23 Nov	—
Spend	≤ ₦11m	Phase 1 ≤ ₦23m

The member and coded-sales targets assume today's sales volume. Reset them once the baseline is locked on 6 November.

IF SOMETHING SLIPS

Risk	Fallback
Sterling says no to stickers	Put the code on a card in the bag at the point of sale, or on the reseller invoice.
Sticker delivery slips	Hand-numbered verification cards for founding members; code the first 2,000 packs only.
ARCON vetting runs long	Start with unpaid member content; paid creator posts wait for approval.
No community lead by 23 Nov	The interim owner runs the soft launch; move the public launch, not the Glow Session.
Baseline data has gaps	Use the last three months and online-store orders; mark the gaps and fill them in January.

MONTH-ONE SPEND

Item	₦m
Pack codes, WhatsApp API and customer database (set-up)	5.0
Micro creator base fees (December cohort)	2.5
Community lead and data support (from 23 Nov)	1.0
Content production and ARCON vetting	1.0
Glow Session #1	0.6
Paid boosts of member content	0.5
Total, of Phase 1's ₦23m	**10.6**

Creator commissions, referral credits and points are paid from sales, on top of this.
